


Gilbert – Ash
Project Newsletter – February 2022



- Since our previous newsletter in December 2021, we are delighted to report on the progress made during the demolition stages;
- We have ongoing movement, vibration, noise and dust monitoring at our site at levels pre-agreed with the Council;
- Please refer to the Project Website for further information - <https://park-street.co.uk/>

Progress Update

Our site accommodation and welfare is located at nr17 Park Street. Please feel free to pop by and speak to us if you have any queries.

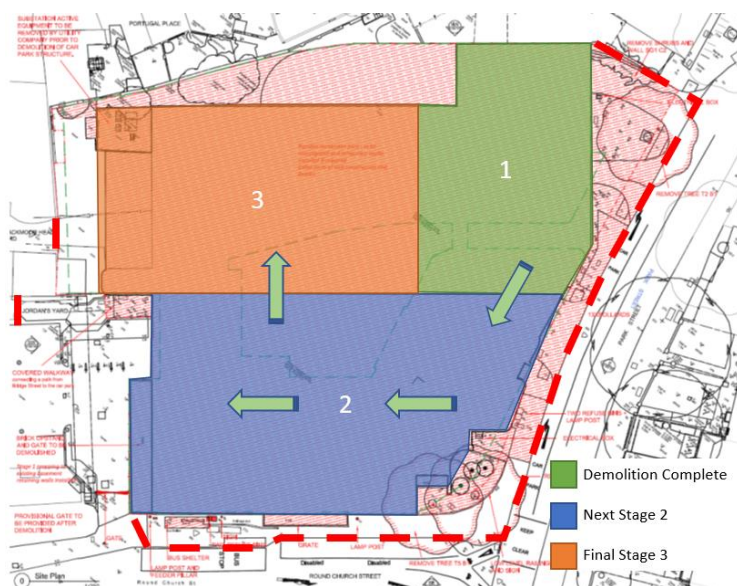

All existing car park services were disconnected and fully removed.

Demolition is progressing and refer to the adjacent diagram.

The structure is being progressively being taken down a bay at a time.

Area 1 in green is complete and the contractor will be moving into zones 2 & 3 in the coming weeks.

Gilbert – Ash
Project Newsletter – February 2022



Demolition jaws pulverising & removing slab sections floor bay at a time




Park Street view of the demolition progress.

Upcoming Planned Works

Planned works in the coming months (February – May 2022)

- Continued demolition of the remaining car park structure from Park Street along Round Church Street and back toward Portugal Place.
- Preparation works ahead of the first Piling visit i.e. piling mat build up and access.
- Commence Piling from May 2022 and to clarify this is a non-percussive method using an auger which drills into the ground. There are no pile driving methods associated with this project.

Overall Project TimeLine

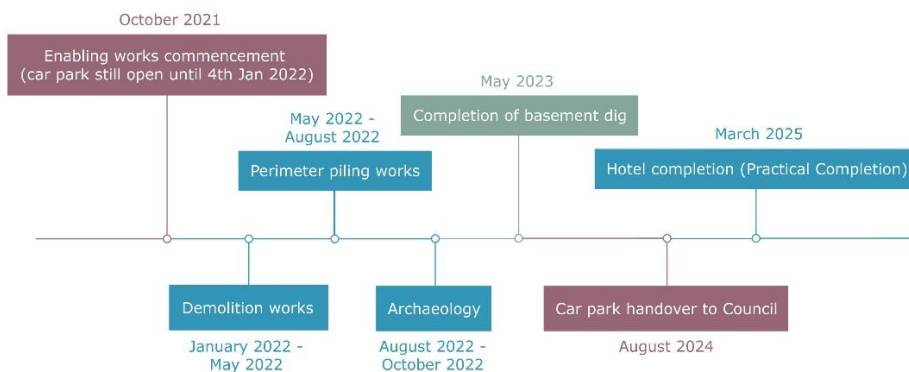



MARICK
PARK STREET - STAYCITY APARTHOTEL
CAMBRIDGE, CB5 8AS

Gilbert – Ash
Project Newsletter – February 2022

Health and Safety

Gilbert-Ash take the health and wellbeing of all those engaged with the project extremely seriously whether they are visitors, neighbours, supply chain members, operatives, managers, and members of the public.

During the next stages we will continue focusing on the demolition activity, we will be continuing to secure the relevant work areas to ensure they are safe in close proximity to members of public. Our banksmen will have a continued presence on the roadways to direct our logistics and assist with coordination of other vehicles in the proximity of the site. Logistics will continue to be 'just in time' delivery only.

We are mindful of our proximity to members of public, sensitive residential and business properties as well as the Primary School. We will be working with all to maintain a safe environment around the site area.

Community Liaison

Gilbert-Ash would like to take this opportunity to thank you, the residents and neighbours for your support and patience whilst the work is progressing. We will endeavour to minimise any disruptions to local businesses and residents during these works but in the interim if you wish to discuss anything regarding the project, please feel free to make contact as below:

Site Contact Details



Martin Douthart
Senior Site Manager

Martin.Douthart@gilbert-ash.co.uk

07736270890



Warren Copeland
Contracts Manager

Copeland@gilbert-ash.co.uk

07791413668
